Ham Lake P18-091 (2018) 167th Ave/Frazier street & 165th Ave

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		TRAFFIC CONTROL	1 day	Mon 7/30/18	Mon 7/30/18	
14		CULVERT END CONTROLS	1 day	Mon 7/30/18	Mon 7/30/18	
2		CLEARING AND GRUBBING	5 days	Tue 7/31/18	Mon 8/6/18	
13		INSTALL SILT FENCE	1 day	Wed 8/1/18	Wed 8/1/18	
17		RELOCATE FENCE	2 days	Wed 8/1/18	Thu 8/2/18	
3		REMOVE MAILBOX & PUT UP TEMP. MAILBOX	1 day	Fri 8/3/18	Fri 8/3/18	
4		SAW CUT CONC. & BIT.	1 day	Fri 8/3/18	Fri 8/3/18	
5		CONCRETE & ASPHALT D.W. REMOVALS	1 day	Mon 8/6/18	Mon 8/6/18	
6		PIPE INSTALL	8 days	Tue 8/7/18	Thu 8/16/18	
7		COMMON / MUCK / CHANNEL & POND EXCAVATION	8 days	Thu 8/9/18	Mon 8/20/18	
8		INSTALL CONCRETE CURB & GUTTER / DRIVEWAYS	2 days	Tue 8/21/18	Wed 8/22/18	
9		FINAL SHAPE ROAD	3 days	Thu 8/23/18	Mon 8/27/18	
10		PAVE BASE	2 days	Tue 8/28/18	Wed 8/29/18	
11		RAIN GARDEN ESTABLISHMENT	2 days	Thu 8/30/18	Fri 8/31/18	
12		TURF ESTABLISHMENT	2 days	Mon 9/3/18	Tue 9/4/18	
15		INSTALL MAILBOX	1 day	Wed 9/5/18	Wed 9/5/18	
16		INSTALL SIGNS	1 day	Thu 9/6/18	Thu 9/6/18	

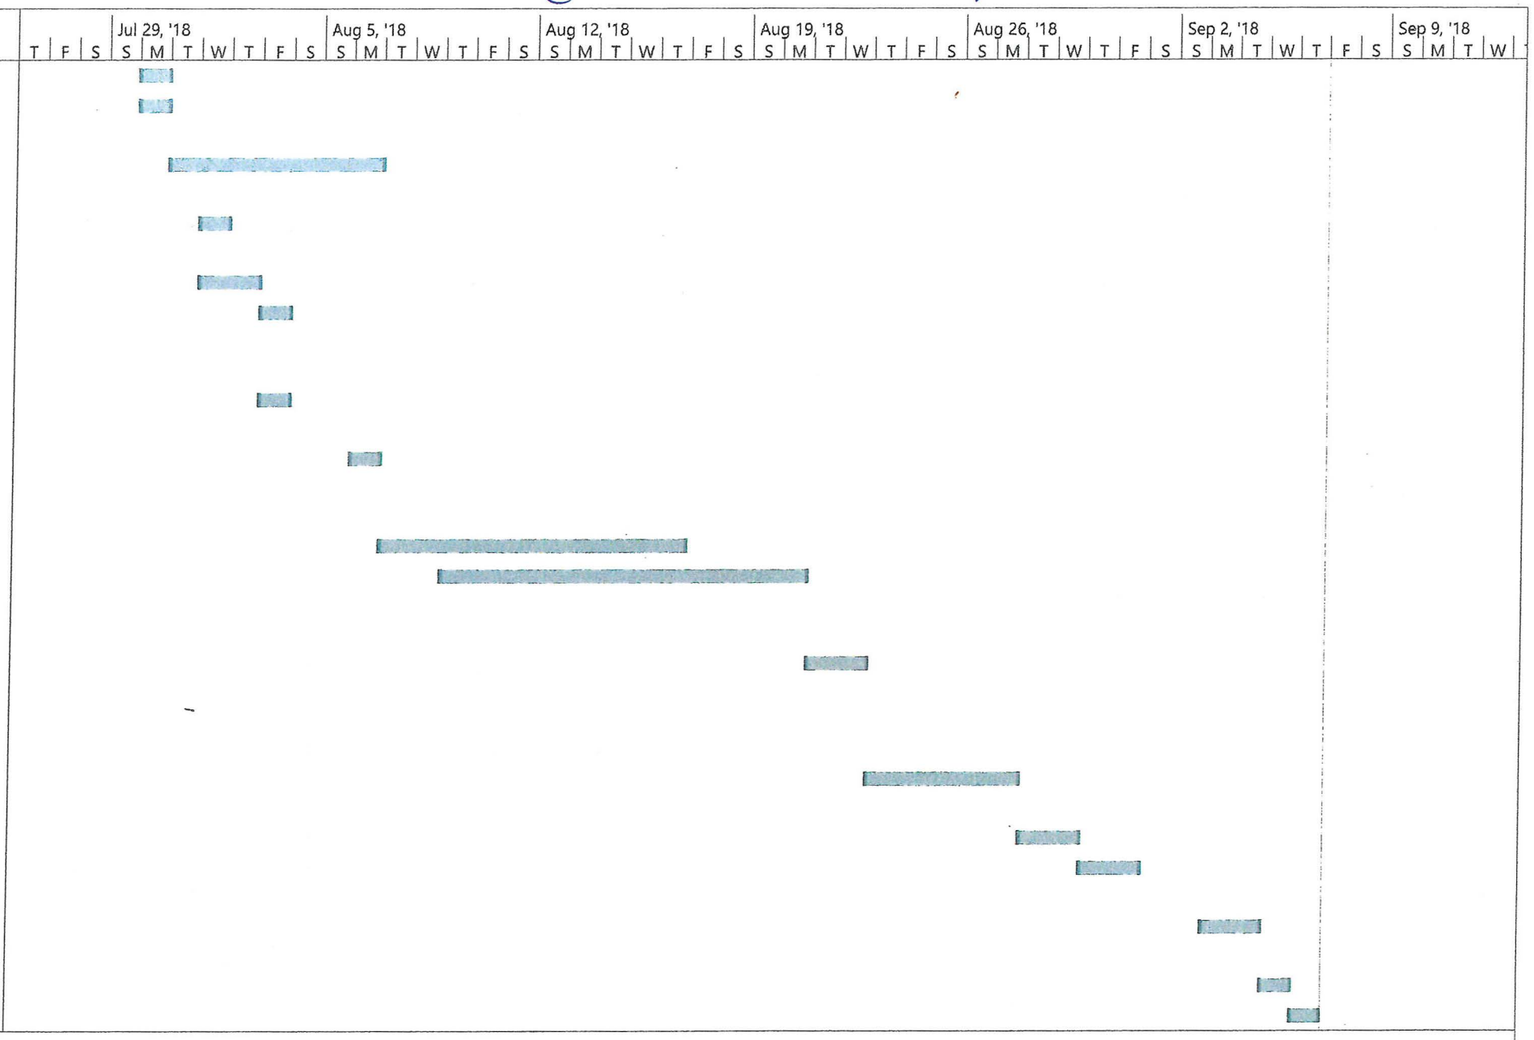

Project: HAM LAKE SCHEDULE 201
Date: Mon 7/23/18

Task	Project Summary	Manual Task	Start-only	Deadline			
Split	Inactive Task	Duration-only	Finish-only	Progress			
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress			
Summary	Inactive Summary	Manual Summary	External Milestone				
