Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Quali	Start	Finish
24-1 Ham Lake		179.0d	179.0d	0%		02-Sep-25	18-May-26
24-1.1 Milestone		179.0d	179.0d	0%		02-Sep-25	18-May-26
M1000	Project Start	0.0d	0.0d	0%		02-Sep-25	
M1010	Pipe Crew 1 Start	0.0d	0.0d	0%		02-Sep-25	
M1020	Pipe Crew 1 Finish	0.0d	0.0d	0%			02-Sep-25
M1090	Grading Crew 1 Start	0.0d	0.0d	0%		18-Sep-25	
M1100	Grading Crew 1 Finish	0.0d	0.0d	0%			24-Nov-25
M1130	Adjusting Crew Start	0.0d	0.0d	0%		11-Nov-25	
M1140	Adjusting Crew Finish	0.0d	0.0d	0%			17-Nov-25
M1150	Project Finish	0.0d	0.0d	0%			18-May-26
M1200	Winter Suspension	0.0d	0.0d	0%		05-Dec-25*	
M1210	Spring Start up	0.0d	0.0d	0%			04-May-2
24-1.2 Construction		179.0d	179.0d	0%		02-Sep-25	18-May-26
A1000	Mobilization	1.0d	1.0d	0%		02-Sep-25	02-Sep-25
A1010	Traffic Control	1.0d	1.0d	0%		03-Sep-25	03-Sep-25
A1020	Clearing & Grubbing	6.0d	6.0d	0%		04-Sep-25	11-Sep-25
A1030	Erosion Control	3.0d	3.0d	0%		12-Sep-25	16-Sep-25
A1040	Saw Cutting	1.0d	1.0d	0%		17-Sep-25	17-Sep-25
A1050	Removals	1.0d	1.0d	0%		17-Sep-25	17-Sep-25
A1060	Common Excavation	3.0d	3.0d	0%		18-Sep-25	22-Sep-25
A1070	Common Embankme	6.0d	6.0d	0%		16-Sep-25	23-Sep-25
A1080	Common Pond	9.0d	9.0d	0%		24-Sep-25	06-Oct-25
A1090	Common Embankme	6.0d	6.0d	0%		01-Oct-25	08-Oct-25
A1100	Storm Sewer	20.0d	20.0d	0%		02-Oct-25	29-Oct-25
A1110	Modular Block Wall	10.0d	10.0d	0%		16-Oct-25	29-Oct-25
A1120	Class 5 Agg	4.0d	4.0d	0%		28-Oct-25	31-Oct-25
A1130	Well Abandonment	3.0d	3.0d	0%		30-Oct-25	03-Nov-25
A1140	Curb and Gutter	5.0d	5.0d	0%		04-Nov-25	10-Nov-25
A1150	Bit - Binder	5.0d	5.0d	0%		11-Nov-25	17-Nov-25
A1160	Topsoil - Respread	30.0d	30.0d	0%		14-Oct-25	24-Nov-25
A1170	Restoration	5.0d	5.0d	0%		25-Nov-25	03-Dec-25
A1180	Bit - Surface	5.0d	5.0d	0%		05-May-26	11-May-26
A1190	Paint	5.0d	5.0d	0%		12-May-26	18-May-26

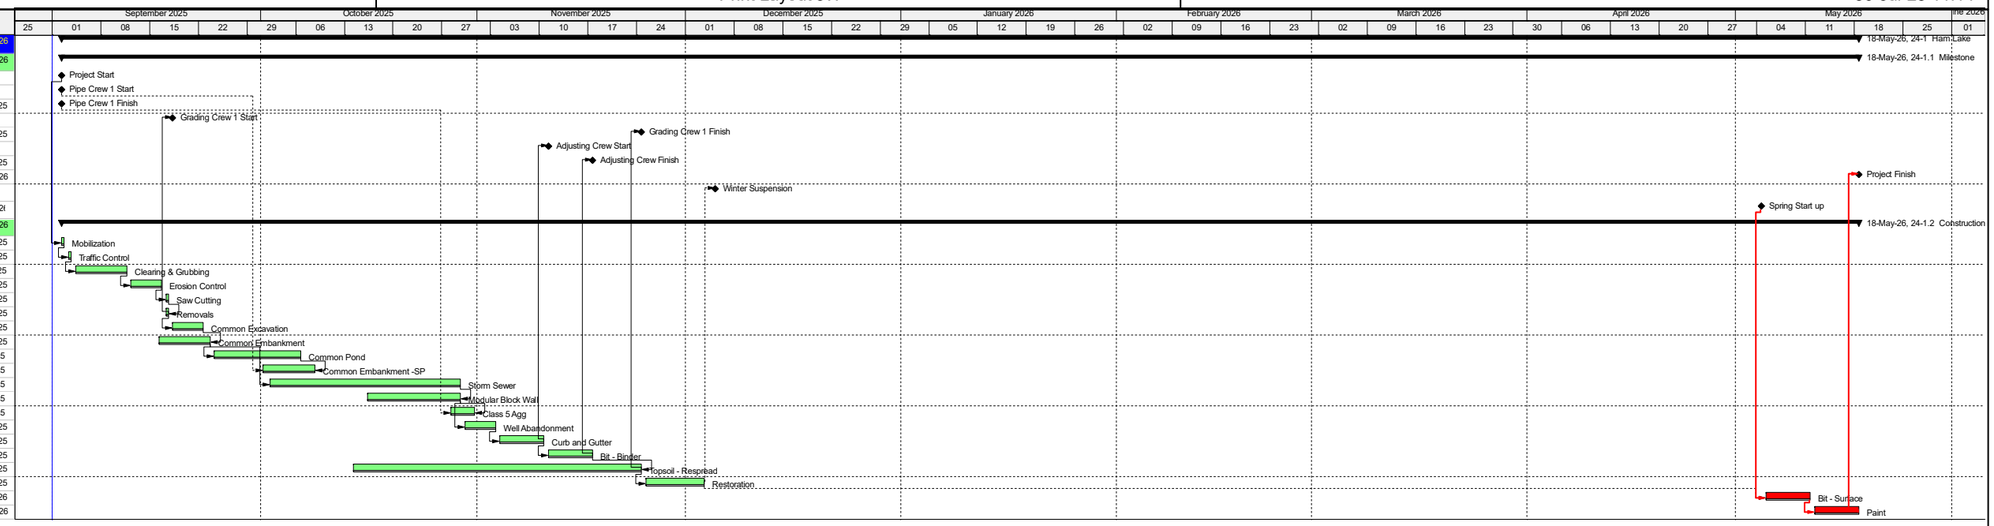

Project Baseline Bar | Remaining Work | Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Oracle Corporation
